


CHAPELCROSS SITE STAKEHOLDER GROUP 29 November 2023

**Richard Murray
Chapelcross Site Director**

Agenda

- [EHSS&Q Performance](#)
- Site News
- Programme Update
- Socio Economic Update
- Questions



EHSS&Q Performance

- TRIR – 0.46, DACR – 0.46
Individual suffered a back injury carrying out a manual handling operation
- No significant events since the last meeting
- MILWEP Part B PPC permit received from SEPA



Site News

Targets for FY 23/24

- 8 Mac and Cobalt Mosaiks retrieved to the ILW store - 8 complete
- 52 CXPP 500l drums filled and transferred to the ILW store - 28 complete
- Dispatch 14 consignments of LLW - 10 completed
- Design completed for the Cooling Tower land remediation - complete
- Commence in-active commissioning of the Zeolite skip retrieval process - target end March 2024
- Deliver £3.5m of asset care improvements - on target

Site News

Recruitment

New recruits started:

- Site Security Manager
- Deputy Site Security Officer
- 4 Trainee Heath Physics Monitors
- Radiation Protection Assistant

External recruitment currently in progress:

- 2 Senior Project Engineers
- CXPP Production Technician



CXPP Decommissioning – ILW Retrievals



Cave Line ILW Retrievals – Routine Cave Entries in Progress to De-Plant, Size Reduce and Package Legacy Machinery and Associated Equipment

CXPP Decommissioning – ILW Retrievals



CXPP Process Line Enabling Works - C4 Air-Fed Suit Entries Carried Out to Remove Loose Tritiated Waste Items from the Cubicle in Preparation for Active Commissioning

Pond Decommissioning

- Safely retrieved 34 ILW Mosaik DCIC's from the Ponds
- All Mosaiks have now been processed through AVDS and are stored in the ISF



- POCO work has commenced and is well underway with a large amount of equipment removed making way for Zeolite equipment installation



Pond Decommissioning

- Zeolite equipment scheduled for installation early January 2024
- Zeolite Inactive Commissioning scheduled March 2024



Pond Decommissioning

- MAETP installation is complete
- Inactive commissioning close out planned for early December 2023
- Active commissioning January 2024



Cooling Towers Remediation

- Work is ongoing with the strategy for remediation of the cooling tower areas
- Planning permission documentation currently being produced to allow removal of the crushed concrete
- Working closely with NWS to plan to remove the crushed concrete and reuse elsewhere



Waste



- ILW – recovery of all 34 MAC & Cobalt MOSAIKS from Pond 2 to ISF complete
- 23/24 - 9 shipments of LLW from the site (YE target 14)
- Focus on Problematic Legacy Wastes including Oils & Liquids and Graphite. Two Oils & Liquids shipments completed



Waste




Other Legacy Waste Progress:

- Redundant Scaffold (in ISOs)
- Inspecting Legacy Waste Half Height ISOs
- Shipping non-radioactive legacy wastes (redundant trailer)



Asset Care

- Glazing replacement has commenced on the reactors. This is part of a 5 year programme which includes all 4 reactor buildings

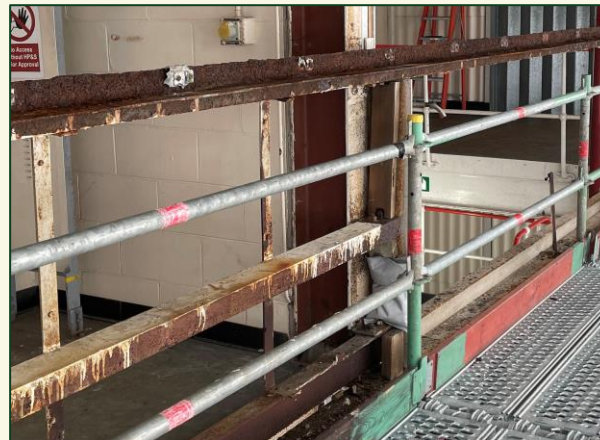

Socio-Economic Update

- No new applications for funding



Any Questions . . .

