



Magnox

Magnox Ltd is owned by the Nuclear Decommissioning Authority

Dungeness A Site Report to Site Stakeholder Group – February 2021

Ian Cuthbert
Site Director




Safety and Compliance

- The site has now exceeded 1,730 days (over 4½ years) since its last Lost Time Accident
- There has been one minor first aid incident since the last report
 - individual cut finger on scaffold gate
- There are currently 127 Magnox staff on site
- The site is currently rolling out a Covid-19 testing facility that site personnel can utilise. This will give extra reassurance to both the site and its workers



Plant and Structures programme update

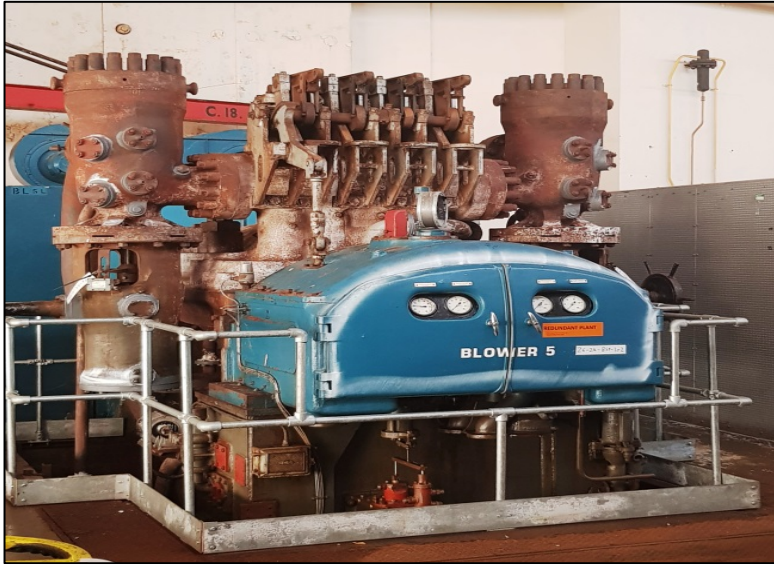

Blower stripped of asbestos – the majority of the exposed steel work would have been lagged in asbestos on all 8 blowers

The last asbestos enclosure out of a total of 163 for the project has now been struck from R1 Ponds and the last fourth stage clearance for reoccupation has been issued by Element

Erith completed all site works and left site on 4 February 2021

Ponds programme update

- Remediation of the blocked sludge line
- Processing the remaining two sludge drums
- Waste processing and back out works within each pond



“Haki” staircase installed to enable easier access

Asset Care projects

- In this financial year (2020/21) there are 27 work packs being worked on with a forecast value of approximately £1.5M
- The site continues to reduce and remove the number of legacy scaffolds
- Covid-19 arrangements have been put in place, to protect the staff, contractors and visitors to the site, to ensure social distancing can be maintained



Asset Care projects

- Over the Christmas break high winds (*Storm Bella*) caused significant damage to the reactor building 2B-side drum house roof. Loose materials and debris have been secured.
- Arrangements are being made to remove the remainder of the roof and install a new roof




What next...

- Our priorities continue to be safe asset care – ensuring the fabric of the buildings and plant do not degrade to present a hazard to our workforce or the environment
- This year:
 - remove external ventilation and ducting from Dungeness A Medium Active Laboratory (DAMAL)
 - R1 and R2 pond back out works
 - security gate upgrade and repairs
 - Modular Active Effluent Treatment plant (MAETP) active commissioning



DAMAL building -
preparing duct removal

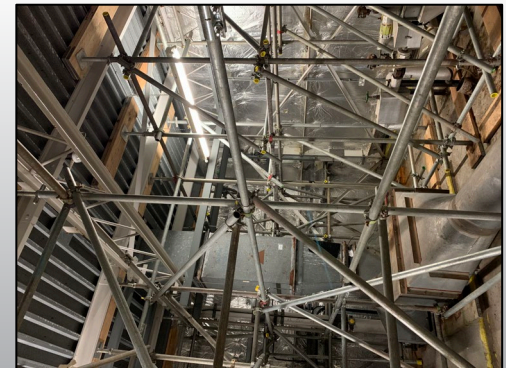

Magnox Socio-economics – 2020/21

Magnox Soc-ec Scheme £1,020,035 of funding available from 01/04/20

- £25,000 made available to support local Covid-19 initiatives at each site. £300,000 committed from the overall scheme. F&HDC has £11,500 remaining
- Total funding for Dungeness A to date £49,919
 - Good neighbour sub-total £2,919
 - Small projects £2,000
 - Medium projects £45,000
- Cut off date for this financial year is 26/02/21

For further information and to check eligibility, go to: <https://www.gov.uk/government/collections/magnox-working-with-our-communities>

For applications under £1,000 contact Eirian Vaughan-Lewis: Eirian.vaughan-lewis@magnoxsites.com

Applications over £1,000 Contact Haf Morris: Haf.e.morris@magnoxsites.com or tel: 07912799820

Thank you

- Any questions?

