# Welcome

**Sizewell A & B Stakeholder Group**

Please:

- Be courteous to one another
- Do not talk over other people
- Respect every viewpoint
- Wait for the microphone before talking



NDA | NRS Nuclear Restoration Services

# Presentation to Site Stakeholder Group

## Sizewell A Site


## Alan Walker
## Site Director, Sizewell A site


11/03/2026

Nuclear Restoration Services

# Sizewell A & B Stakeholder Group Meeting Agenda – 11/03/2026

## AGENDA

Venue: Leiston Town Athletic Association (LTAA), Victory Road, Leiston IP16 4DQ

9:00am for 9:30am start, refreshments will be served

**1. Welcome** - Apologies for absence and declarations of interest

**2. Sizewell A Reports**

Alan Walker - Site Director, NRS
ONR Report – There has been no inspection on site since last meeting. Any questions will be forwarded for response.
James Heavingham - Environment Agency

**3. Sizewell B Reports**

Robert Gunn – Station Director, EDF
David Prescott - Site Inspector, Office for Nuclear Regulation. There has been no inspection on site since last meeting. Any questions will be forwarded for response.
Themis Kantara - Environment Agency

**Refreshment BREAK and networking**

**4. NDA Report** (including NGO Forum) – John McNamara

**5. Matters arising and questions from Minutes of 27th November 2025 and Action** Tracker (not already included in reports above)

**6. Chair Report (including preparations for 20th Anniversary celebration and next meeting)**

**7. SSG Constitution and consideration of amendments**

**8. Co-option of Members and Confirmation of any new Members**

**9.. Any other business**

Date of next meeting: **TBC**

# Safety, Compliance & Environment

**WHATS GONE WELL:**

- ✓ Safety – Total Recordable Incident Rate (TRIR) and Days Away Case Rate (DACR) Remain at ‘0’
- ✓ Successful Security Demonstration Exercise 'Adequate' rating achieved
- ✓ Full Review completed for the SZA Environmental Monitoring Programme
- ✓ Physical completion of Turbine Hall demolition project – Principal Contractor demobilised

**LEARNING**

- ❖ Loose material found in our active effluent plant during re-configuration works
- ❖ Capturing Learning for Mutually Agreed Voluntary Exit (MAVE)
- ❖ Monitoring a slight increase in defect related events


**LOOK AHEAD:**

- ➢ Human Performance Campaign – Year long focus on 'Error Prevention Tools
- ➢ Aqueous discharge inspection
- ➢ Piloting a 'Sustainability' study to develop wider company processes
- ➢ A programme of volunteering days being established
- ➢ Two 'Work Experience' weeks planned

# 2025/26 - Asset & Infrastructure Care


**Selection of works completed or in progress:**

- Trunk Radio System Replacement – in progress
- Welfare Building Fire Door replacement – in progress
- Asbestos Remediation – dedicated team continues
- Site Wide Drains Survey – complete
- Reactor Building Weather Envelope Cladding Inspection - in progress

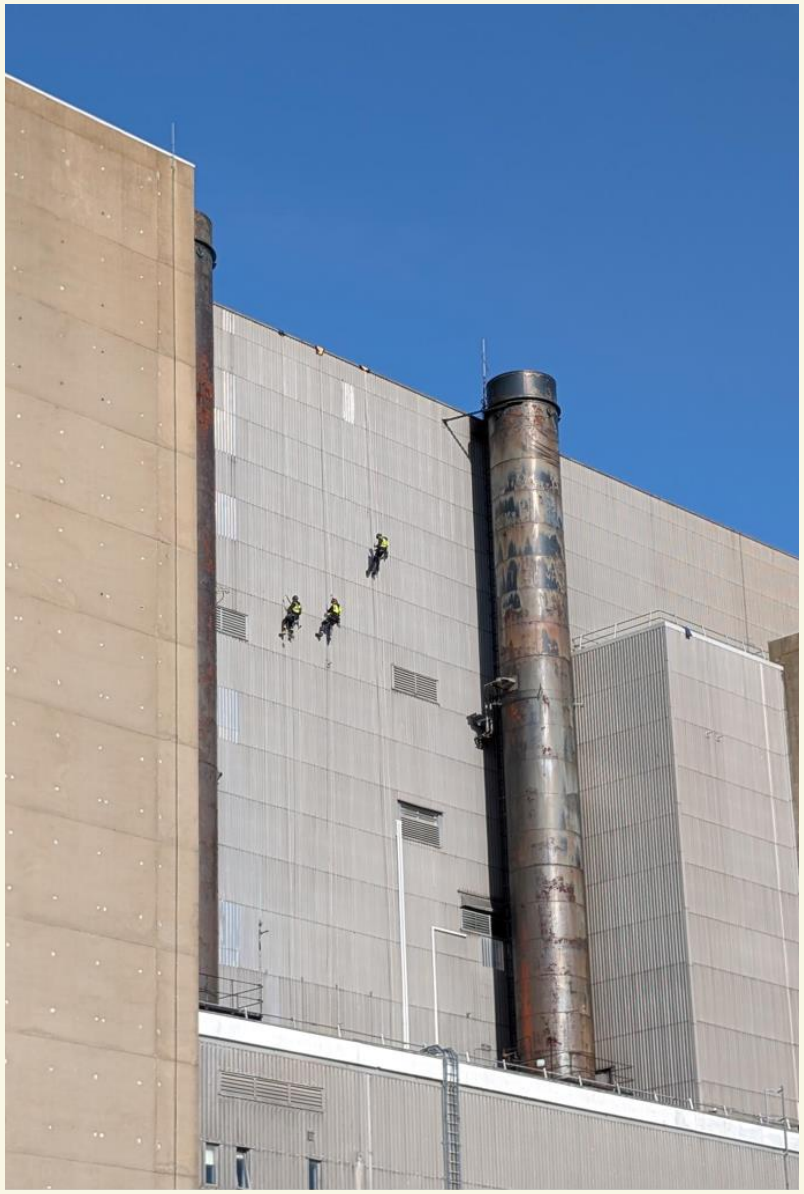


# 3 month look ahead – Asset & Infrastructure Care

- Trunk Radio System Replacement – continuation
- AETP Sub change welfare improvements - to continue
- Ponds roof refurb/replacement - out to market
- Offshore Structures – out to market

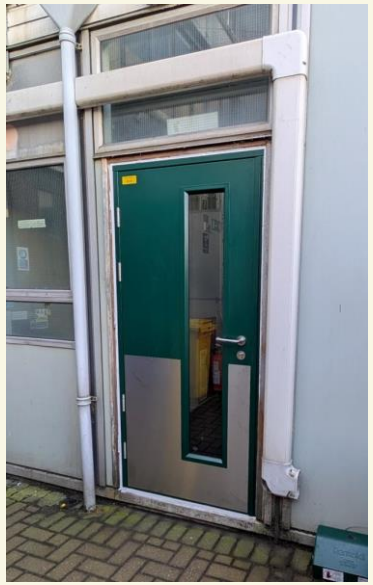



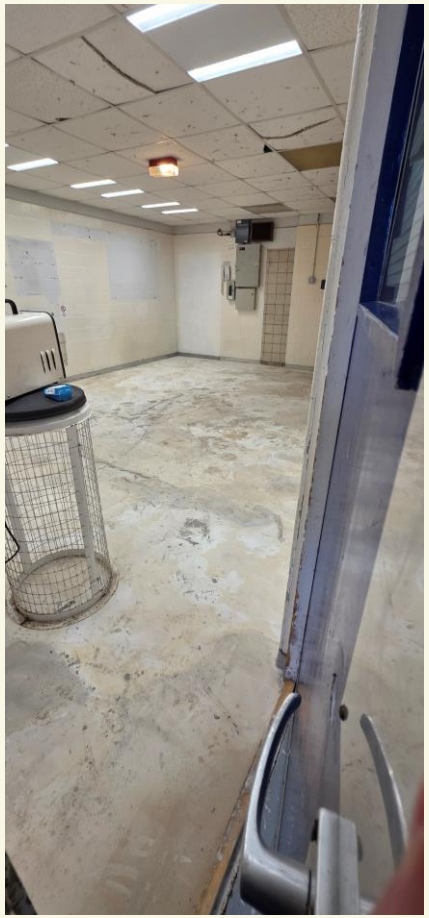





# Waste Operations – Sizewell

**Success:**
- Ponds Skips Waste Processing: 10,781kg of ponds de-plant waste
- Programme ~ 61% complete
- ~ 91% diversion rate achieved.

- Skip Characterisation work progressing with external laboratory
- Enabler for the final disposal of significant radiological waste stream
- LLW skips size reduced

**Consignments:**
Eight rad waste consignments this year
- 3 x Metal Treatment
- 3 x Incineration
- 2 x VLLW

Application of Waste Hierarchy and optimisation of NWS supply chain



# 3 month look ahead – Waste Operations

- Waste – Skip mast de-plant
- Waste Inventory Management System (WIMS) Implementation
- Annual Hazardous Waste Consignment
- Self Perform Opportunity (legacy waste reduction)





**Waste Projects Readiness & Support**

- FED
- ILW Facility
- Ponds Roof Repair

# Sizewell A Programmes

| Ref | Project Description | 26/27 | 27/28 | 28/29 | 29/30 | 30/31 |
|---|---|---|---|---|---|---|
| 27601 | FED | Scheme | | | D&B Contract | |
| 27302 | Boiler Houses Isolations | Complete Isolations | | | | |
| 27303 | Boiler House Asbestos & Ancillary Plant Removal | Commercial & Sampling | | | Contract Let & Works | |
| 27201 | Ponds & AETP Decommissioning | Continuous Execution Including Asbestos Removal | | | | |
| 27639 | ILW Facility | Design & Commercial | | Contract & Construction | | |
| 27638 | Waste Enablers | | | | Sampling | |
| 27606 | Sludge and Sand | | | | | Commence |
| 27609 | Conditioning Plant D&B | | | | | Commence |

# Turbine Hall Deplant and Demolition


- 15,629 Tonnes of crushed aggregate transferred to Sizewell C
- 12,000te of Metal Recycled
- Over 95% recycle rate for the Project
- Over £3M income received from scrap sales which will be used for further decommissioning works
- 186,000 hours of Person Hours of deplant and demo works without any significant safety incident





# Boiler Isolations Progress – 3rd Boiler Cell - R2CD



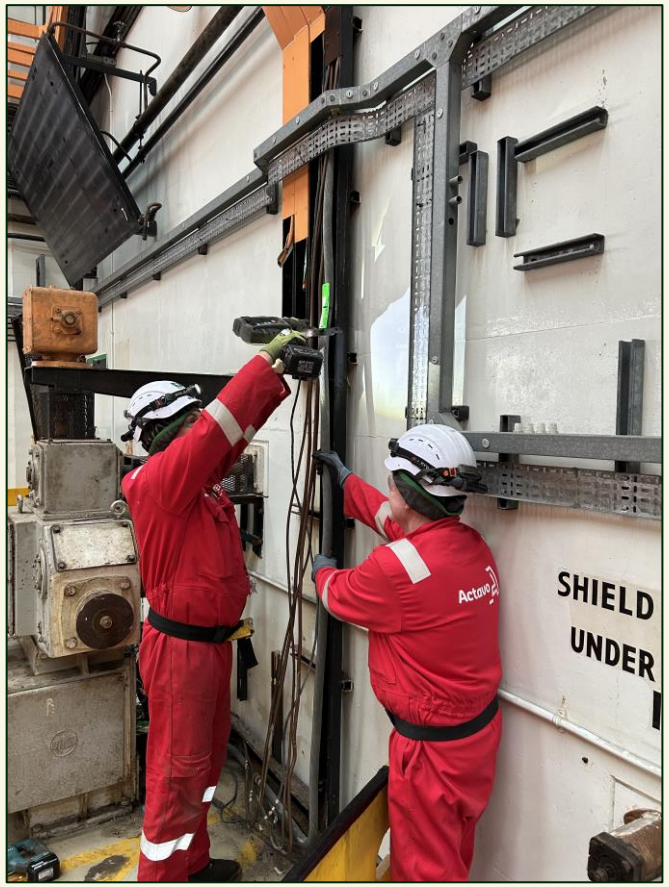


1st Boiler Cell – R1AB Boiler Isolations – 100% Complete
2nd Boiler Cell - R2AB Boiler Isolations – 100% Complete
3rd Boiler Cell - R2CD Boiler Isolations – 64% Complete
4th Boiler Cell – R1CD Boiler Isolations – 0 % - Not started

# Ponds Decommissioning



## Ponds 5Te Hoist Defect Repairs

The 5te Hoist required to transfer skips into the ponds for size reduction and processing requires defective maintenance.

Repair specification has been submitted to the supply chain for quotation. Surveys and Asbestos clean are in progress, which will enable repair works.





## AETP Reconfiguration

Installation of non-intrusive pipe runs, strainers and pumps completed. An additional commissioning recirculation line is required for internal quality checks prior to active commissioning.

Additional recirculation line has been designed, and installation will be progressing within the next month.



# 3 month look ahead – Decommissioning

***Turbine Hall***:
- Contract and Project closeout

***Ponds:***
- 5 Tonne hoist tenders returns, assessment and contract let
- Contractor mobilisation
- Asbestos cleans and rail alignment surveys completed

***AETP:***
- Install new recirculation line
- Complete inactive commissioning
- Commission control and instrumentation equipment
- Prepare for Active Commissioning phase

***ILW Facility:***
- Complete initial change control for insertion into the Mission Plan
- Gain sanction to progress with the Scheme Design

# Sizewell A applications 2025-2026

## Sizewell A funded projects: £123,294.07 - A total of 4 projects supported in FY25/26










### 2 Projects above £2,000 have been supported

**Enhanced Youth Employment Service (YES) – £95,000.00**
Funding has allowed The Youth Employment Service (YES) to support 16–24-year-olds in East Suffolk progress into education, employment or receive training through personalised in-person and online support.

**Museum Director – £25,400.00**
Funding has allowed Long Shop Museum to carry the museum into a new digital-hybrid age, increasing its audience, improving accessibility, and developing its network of community support services and activities.

### 2 Good Neighbour projects have been supported

**Leiston Youth Football Club - £1,995.07 –** Winterproof Kit

**Tunstall Juniors Netball Club - £899.00 –** Matchday Kit

For further information visit: NRS working with our communities - GOV.UK (www.gov.uk)

# Thank you

Any questions?

